

# Stakeholder Notice

## DTB End of Trip Bike Storage Facility (EOTBSF)


STK-N Rev 2  
Date 7 November 2025



As part of the Domestic Terminal Carpark Expansion Project (DTBP2X), construction works for the End of Trip Bike Storage Facility (EOTBSF) will be undertaken by contractor INTREC Management from Monday, 10<sup>th</sup> of November 2025 to Sunday 16<sup>th</sup> of November 2025, between 6:30am and 2:30pm. These works will take place in the area below.

## Location

**Alpinia Drive (Garden Bed at the bottom of P2 Travelator)**

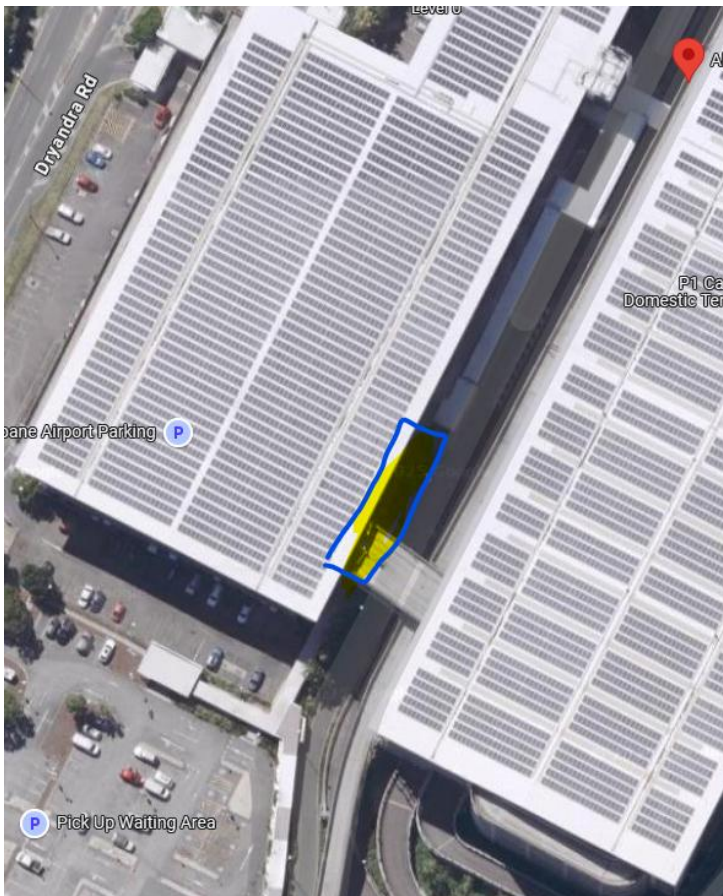



### Day 3 – Wednesday 12<sup>th</sup> of November

**Time: 6:00am – 3:00pm**

- Access panel and FC floor edging Installation
- Modular Installation & Delivery
- Services rough in
- Traffic management setup (6:00am – 3:00pm)

### Day 4 – Thursday 13<sup>th</sup> of November

**Time: 6:00am – 3:00pm**

- Modular Installation
- Formwork and reinforcing Steel to Northern ramp
- Services rough in
- Traffic management setup (6:00am – 3:00pm)

### Day 5 – Friday 14<sup>th</sup> of November

**Time: 6:00am – 3:00pm**

- Modular Installation
- Pour concrete to Northern ramp
- Services rough in
- Traffic management setup (6:00am – 12:00pm)

### Day 6 – Saturday 15<sup>th</sup> of November

**Time: 6:00am – 3:00pm**

- Modular Installation
- Traffic management setup (6:00am – 3:00pm)

### Day 7 – Sunday 16<sup>th</sup> of November

**Time: 6:30am – 3:00pm**

- Modular Installation
- Traffic management setup (6:00am – 3:00pm)

## Impacts

- **General Construction Noise:** Expect typical construction noise during the upgrade process, which may include sounds from machinery, drilling, and other construction activities.
- **Traffic Control Measures:** Traffic control and diversion in place for duration of construction works. Traffic control measures to be removed daily on completion of works.
- **Services:** Services trades working outside of hoarded areas intermittently along footpath (shown in location above) will undertake works in a safe manner for contractors and the public, and any disruption/inconvenience to the public will be minimized through management of safe practices.

## Project Contacts

### KEY CONTACTS BAC

Senior PM / Project Lead  
Craig Mapperson  
0407 544 161  
[craig.mapperson@bne.com.au](mailto:craig.mapperson@bne.com.au)

**Airport Duty Manager contactable 24/7**  
**07 3406 3171**

### KEY CONTACTS INTREC

Project Manager  
Josh Southwell  
0422 769 164  
[Josh.Southwell@intrec.com.au](mailto:Josh.Southwell@intrec.com.au)

Project Engineer  
Taylor French  
0411 202 229  
[Taylor.french@intrec.com.au](mailto:Taylor.french@intrec.com.au)

Site Manager  
Tim Hendry  
0434 421 926  
[Tim.Hendry@intrec.com.au](mailto:Tim.Hendry@intrec.com.au)
